


ID	Task Name	Duration	Start	Finish	Predec	Resource Names	27 Sep '10							4 Oct '10					
							S	S	M	T	W	T	F	S	S	M	T	W	
1	<b>Projekt Tréner mentálnych schopností</b>	<b>65 days?</b>	<b>Mon 27.9.10</b>	<b>Fri 10.12.10</b>															
2	<b>Pred analýzou</b>	<b>6 days?</b>	<b>Mon 27.9.10</b>	<b>Sat 2.10.10</b>															
7	<b>Analýza</b>	<b>14 days?</b>	<b>Mon 4.10.10</b>	<b>Tue 19.10.10 2</b>															
25	<b>Návrh</b>	<b>10 days?</b>	<b>Wed 20.10.10</b>	<b>Sat 30.10.10 7</b>															
26	<b>Funkcionálny návrh</b>	<b>10 days?</b>	<b>Wed 20.10.10</b>	<b>Sat 30.10.10</b>															
27	Návrh funkcionality, UML prípady použitia	3 days	Wed 20.10.10	Fri 22.10.10	11;15;	OU													
28	Návrh grafického rozhrania	4 days	Sat 23.10.10	Wed 27.10.10	27	PB;GD													
29	Návrh štruktúry hier	4 days	Sat 23.10.10	Wed 27.10.10	27	PB;GD													
30	Finalizácia návrhu funkcionality	3 days?	Mon 25.10.10	Wed 27.10.10		OU													
31	Schválenie a pripomienkovanie návrhu funkcionality	3 days	Thu 28.10.10	Sat 30.10.10	30	MK													
32	<b>Architektonický návrh</b>	<b>10 days?</b>	<b>Wed 20.10.10</b>	<b>Sat 30.10.10</b>															
33	Výber technológií pre implementáciu	0,71 days?	Wed 20.10.10	Wed 20.10.10	22;23;	MB;GD;PB;OU;AL;RS													
34	Návrh logickej architektúry, UML diagramy	6 days	Wed 20.10.10	Wed 27.10.10	33	OU;MB;AL													
35	Hrubý návrh fyzickej architektúry, UML diagramy	3 days	Wed 27.10.10	Sat 30.10.10	34	MB;AL													
36	Návrh databázy, UML modely	3 days	Wed 27.10.10	Sat 30.10.10	34	RS													
37	Finalizácia návrhu	3 days?	Mon 25.10.10	Wed 27.10.10		OU													
38	Schválenie a pripomienkovanie architektonického návrhu	3 days	Thu 28.10.10	Sat 30.10.10	37	MK													
39	<b>Finalizácia dokumentácie</b>	<b>3 days</b>	<b>Mon 1.11.10</b>	<b>Wed 3.11.10 32</b>															
40	Finalizácia dokumentácie k analýze a návrhu	2 days	Mon 1.11.10	Tue 2.11.10	31	RS;OU													
41	Finalizácia dokumentácie k riadeniu	2 days	Mon 1.11.10	Tue 2.11.10		RS;OU													
42	Schválenie a pripomienkovanie odovzdaných dokumentov	3 days	Mon 1.11.10	Wed 3.11.10		MK													
43	<b>Implementácia prototypu</b>	<b>24 days</b>	<b>Thu 4.11.10</b>	<b>Wed 1.12.10 25</b>															
52	<b>Testovanie aplikácie</b>	<b>5 days</b>	<b>Thu 2.12.10</b>	<b>Tue 7.12.10 43</b>															
54	<b>Nefunkcionálne požiadavky</b>	<b>63 days?</b>	<b>Wed 29.9.10</b>	<b>Fri 10.12.10</b>															


Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

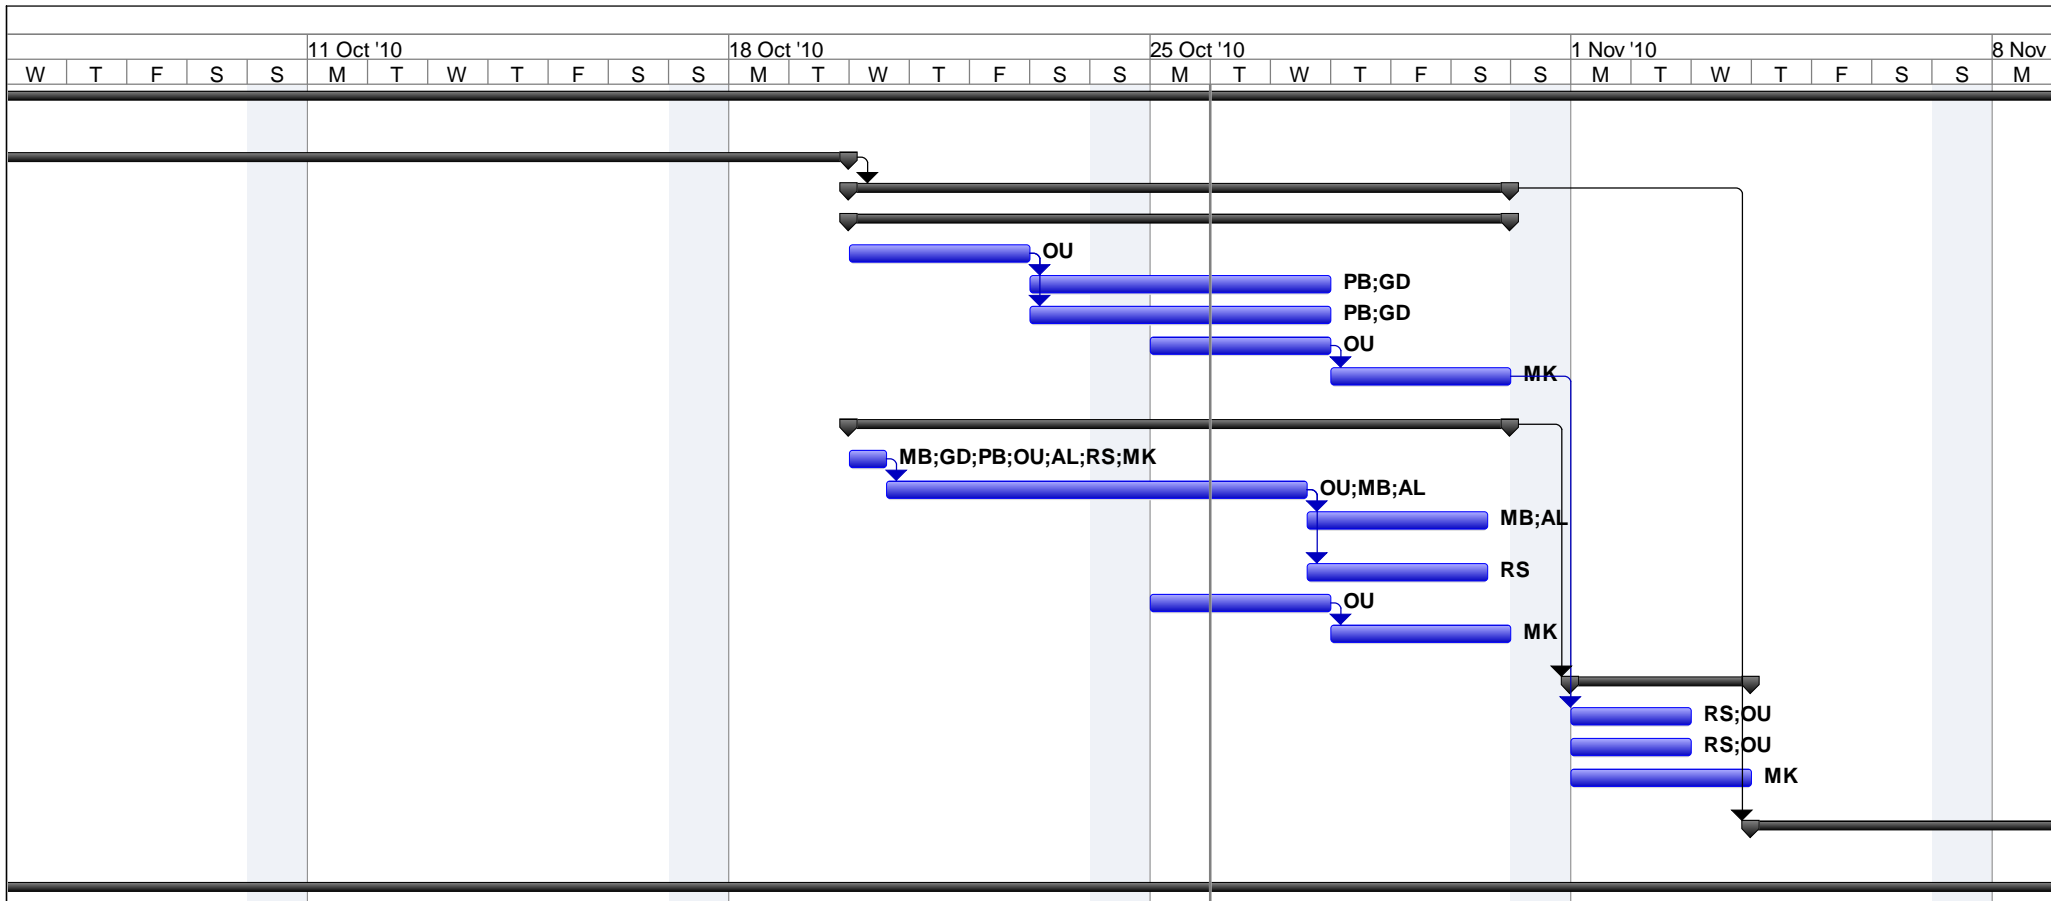

Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	

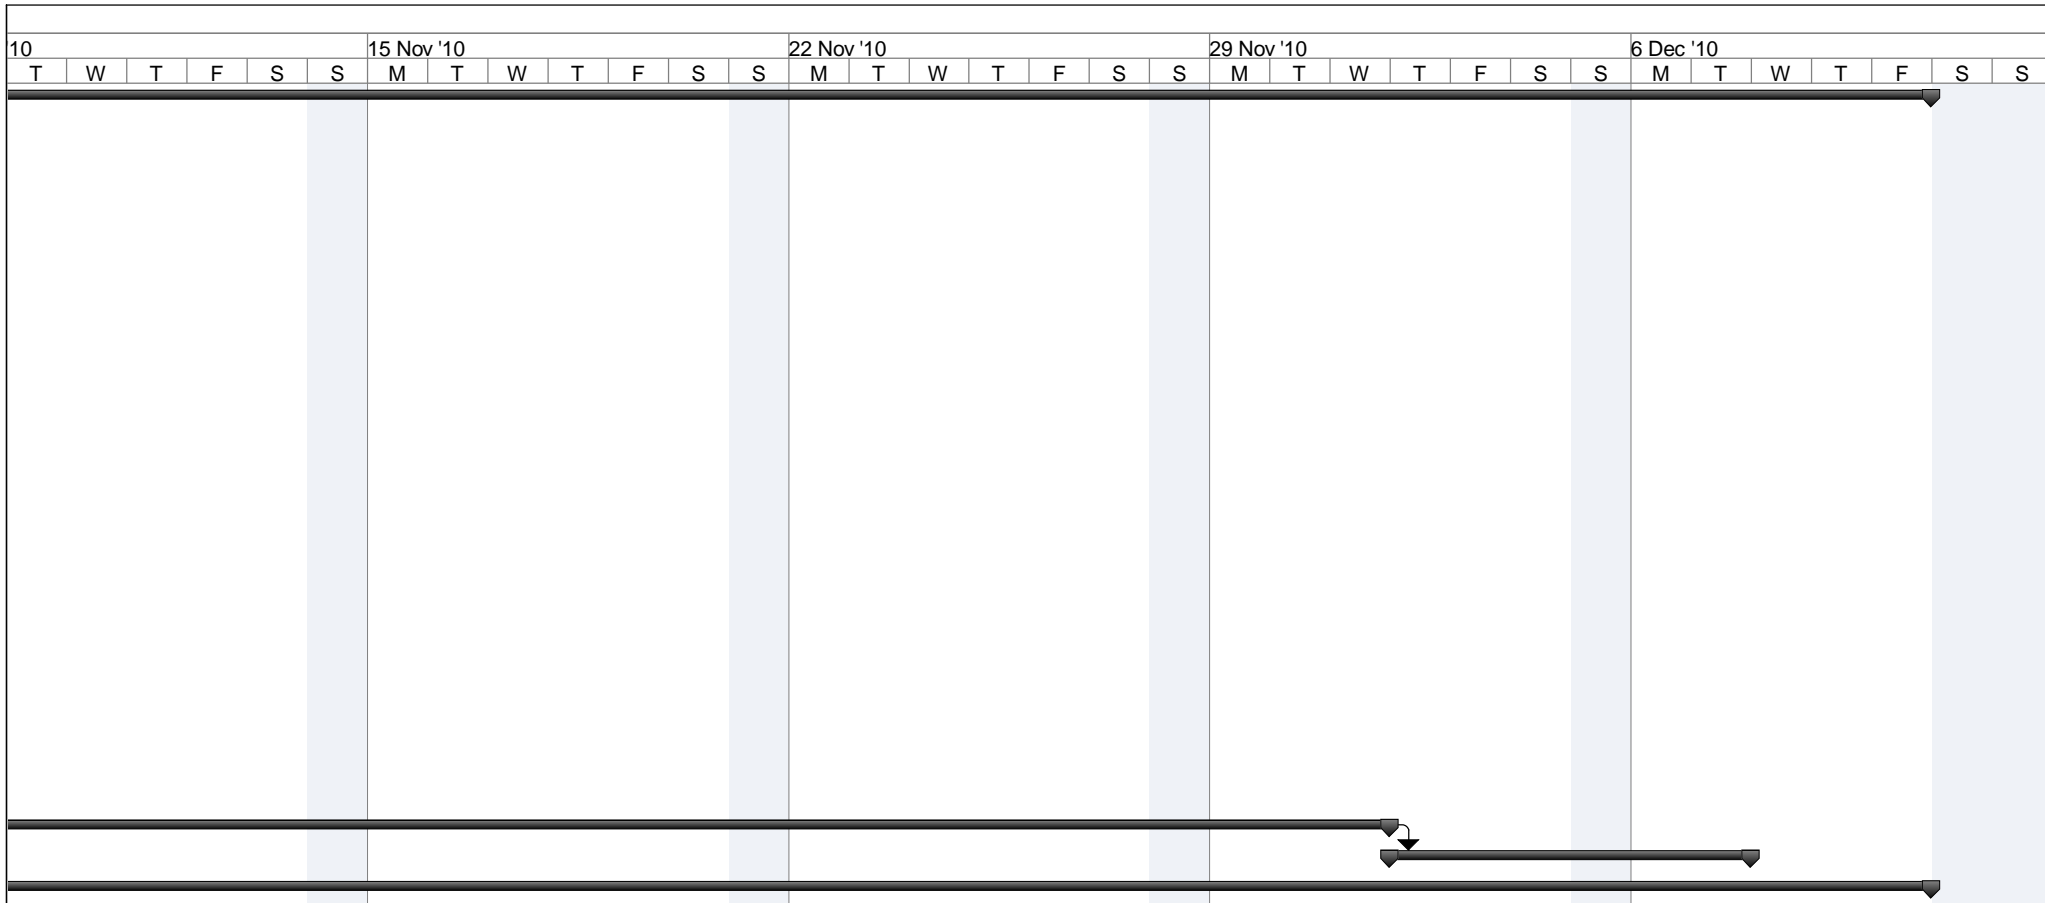

Project: ProjektovýPlán-TrénerMentálny  
Date: Tue 26.10.10

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Progress	
External Tasks		Duration-only		Deadline	
